Project Planning Phase
Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	2 October 2026
Team ID	SWTID-2026-4524
Project Name	Implement Client Script & UI Policy (Incident)
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

Use the below template to create product backlog and sprint schedule

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	UI Policy	USN-1	As an administrator, I can create a UI Policy named High Impact Control on the Incident table with the condition Impact is 1 - High.	3	High	All team members
Sprint-1		USN-2	As an administrator, I can make Assignment group mandatory in the UI Policy and set Reverse if false to true.	3	High	All team members
Sprint-1		USN-3	As an administrator, I can add a UI Policy Action that makes the Urgency field read-only.	2	High	All team members
Sprint-2	Client Scripts	USN-4	As an administrator, I can create an onChange Client Script on the Impact field to set Urgency automatically.	3	High	All team members
Sprint-2		USN-5	As an administrator, I can create an onSubmit Client Script that prevents saving when Assigned To is missing.	3	High	All team members
Sprint-2		USN-6	As an administrator, I can create an onCellEdit Client Script on the State field.	2	Medium	All team members
Sprint-3	Testing	USN-7	As an administrator, I can test every rule, including the reverse condition, list edit blocking and form-based update.	3	Medium	All team members
Sprint-2	Incident form	USN-8	As an incident user, I see Urgency set automatically when I select High impact.	2	High	All team members
Sprint-2		USN-9	As an incident user, I cannot save a High impact Incident without Assigned To.	2	High	All team members
Sprint-3		USN-10	As an incident user, I can still change State from the Incident form.	2	Medium	All team members

Story points and priority are estimates by the team. Sprint-1 total 8, Sprint-2 total 12, Sprint-3 total 5 (25 story points in all).

Project Tracker, Velocity & Burndown Chart: (4 Marks)

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	8	6 Days	5 Oct 2026	10 Oct 2026		
Sprint-2	12	6 Days	12 Oct 2026	17 Oct 2026		
Sprint-3	5	6 Days	19 Oct 2026	24 Oct 2026		

Sprint dates are planned dates. Story points completed and the actual release date are filled in when each sprint ends.

Velocity:

The team plans 25 story points over 3 sprints of 6 days each, so the average velocity is 25 / 3 = 8.33 story points per sprint. The team's average velocity (AV) per iteration unit (story points per day) is:

$$AV = velocity \,/\, sprint\ duration = 8.33 / 6 = 1.39 \text{ story points per day}$$

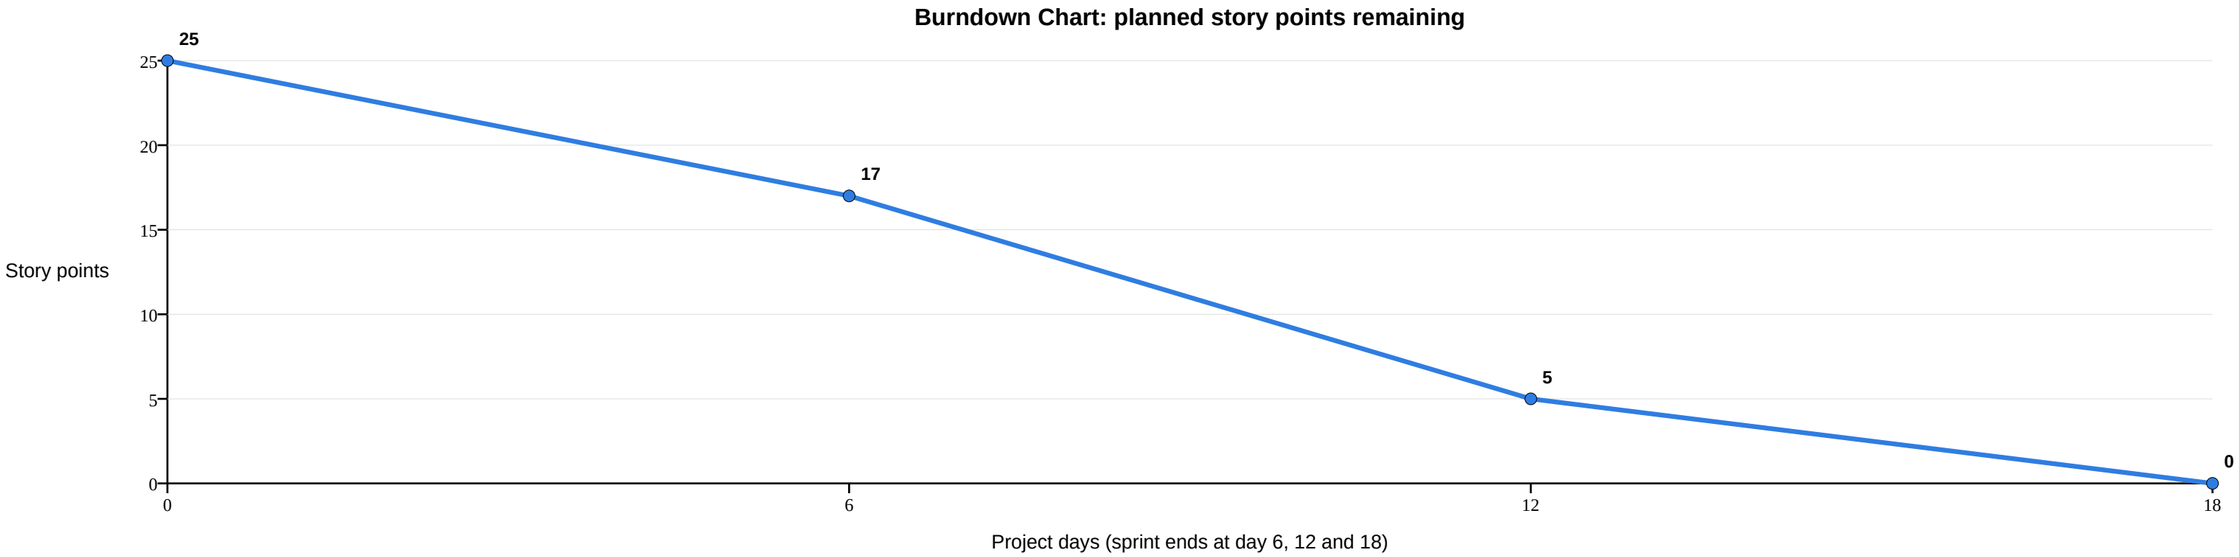

The line shows the planned work left after each sprint (Sprint-1 ends at 17 points left, Sprint-2 at 5, Sprint-3 at 0). The actual line is added from the story points completed in each sprint.

Burndown Chart:

A burn down chart is a graphical representation of work left to do versus time. It is often used in agile software development methodologies such as Scrum. However, burn down charts can be applied to any project containing measurable progress over time.
